




# Tournament Players Parkway

June 2019

Project No. 19-07

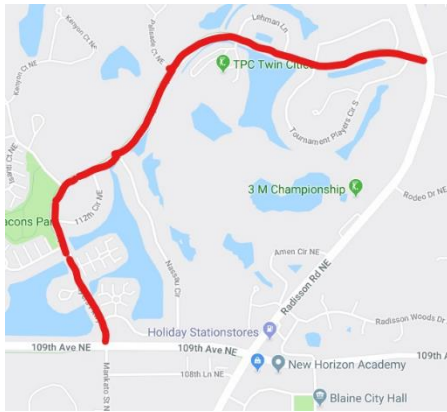

**Location Map**



**Construction**

**Consultant:**

**Sambatek  
Brian Hare**

**Contractor:**

**Park Construction**

**Project Manager:**

**Stefan Higgins**

**Aerial**

## Major Milestones/Completed/Underway

- Project Awarded to Park Construction
- Completed Concrete work.
- Completed Base Asphalt.
- Restoration in process

## Upcoming Work

- Final Restoration and sod.
- Wear course on full roadway
- Signage and striping
- Final Completion Scheduled for 6-21-2019

## Schedule

Week of:	5/13/2019	5/20/2019	5/27/2019	6/3/2019	6/10/2019	6/17/2019
NB/EB - Concrete Work						
NB/EB - Asphalt Recycling & prep						
NB/EB - Base Paving						
SB/WB - Concrete Work						
SB/WB - Asphalt Recycling & prep						
SB/WB - Base Paving						
Wear Course Paving						
Signage, Striping, Restoration						

## Budget Summary

Project Phase	Budget	Expense to Date	% Budget Spent
Design And Construction Support	\$ 673,200.00	\$ 173,303.65	25.7%
Construction	\$ 1,086,241.30		
Engineering, Geotech, Other	\$ 8,800.00		
<b>TOTAL</b>	<b>\$ 1,759,441.30</b>	<b>\$ 173,303.65</b>	
