




Jefferson Street

June 2019

Project No. 18-17

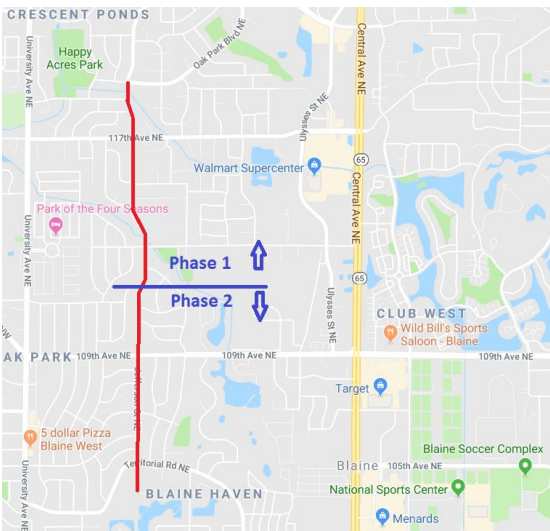

Consultant:

SEH

Greg Anderson

Contractor:

Dressel Contracting

Project Manager:

Stefan Higgins

Project Information

Major Milestones

- Submitted for City Council Award on June 17
- Waiting for final CCWD Permit
-
-

Issues

- Daily Road Closures
- Significant Tree Removals
- Project cut into 2 phases
- Section from 104th to 112th will be in 2020

Schedule

	Q3 2019	Q4 2019	Q1 2020	Q2 2020	Q3 2020	Q4 2020
Storm Sewer Construction						
Street Reconstruction 119th to 112th						
Street Reconstruction 112th to 104th						

Budget Summary

Project Phase	Budget	Expense to Date	% Budget Spent
Design And Construction Support	\$ 821,500.00	\$ 238,034.54	
Construction	\$ 4,446,874.10		
Engineering, Geotech, Other			
TOTAL	\$ 5,268,374.10	\$ 238,034.54	
