

CAPITAL PROJECT WORK

WATER METERS AND ADVANCED METERING INFRASTRUCTURE UPGRADES

Project Manager: Tom Scott
Funding Source: Water Enterprise Fund
Project Budget: \$3,402,300
Schedule: Q3 2017 – Q2 2020
Status: On Schedule

Project Details:

- Replace Meters older than 12 years or 1.4M gallons of use to improve accuracy. Upgrade radio read capability to current supported software communication systems.

Upcoming Work:

Continue replacement/upgrade work by contractor - HydroCorp



iPERL Smart Water Meter

Electromagnetic Flow Measurement System

PHEASANT RIDGE PARKWAY STREET IMPROVEMENTS

Project Manager: Dan Schluender
Funding Source: MSAS & PMP
Project Budget: \$1,300,000
Schedule: Aug 2019- Nov 2019
Status: Plans & Specs Approval 6/2019

Project Details:

- Pavement replacement of Pheasant Ridge Parkway
- Intersection Improvements and Signal Upgrades

Upcoming Work:

- Service Connection switch in progress



Location Map

CAPITAL PROJECT WORK

LEVER STREET IMPROVEMENTS – N OF 125TH


Project Manager: Dan Schluender
Funding Source: Development
Project Budget: \$3,300,000
Schedule: Q2 2019 – Q4 2019
Status: On Schedule

Project Details:

- Construct new road to MSAS Standards with concrete curb and asphalt surfacing. Extension of trunk water, trunk sewer, and storm sewer.

Upcoming Work:

Boulevard restoration
Final wear paving

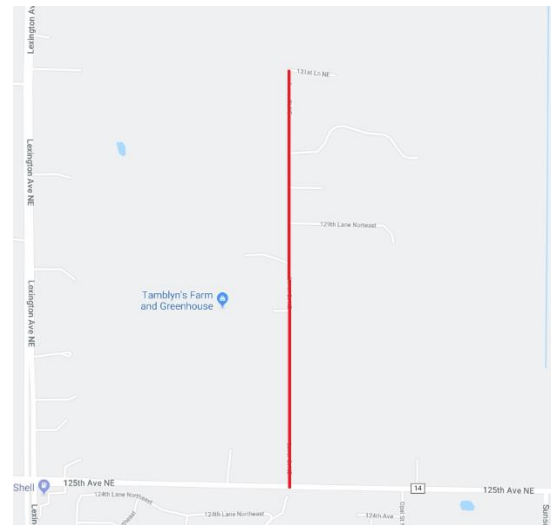

125TH AVENUE RECONSTRUCTION LEXINGTON AVE – OPAL ST


Project Manager: Anoka County Hwy Dept
Funding Source: Federal Pavement Preservation
Project Budget: \$2,100,000
Schedule: Aug 2019- Nov 2019
Status: On Schedule

Project Details:

- Widen to four lane divided highway.
- Median construction
- Signal installation at Lever St

Upcoming Work:

- Westbound Traffic Detour begins June 17

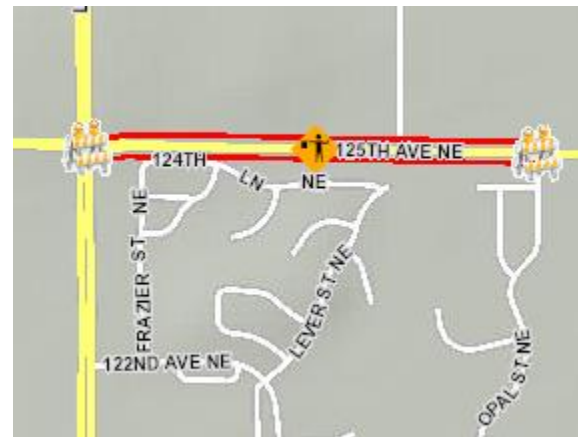

Location Map
