




93rd Ave/Cloverleaf Parkway

June 2019

Project No. 18-18

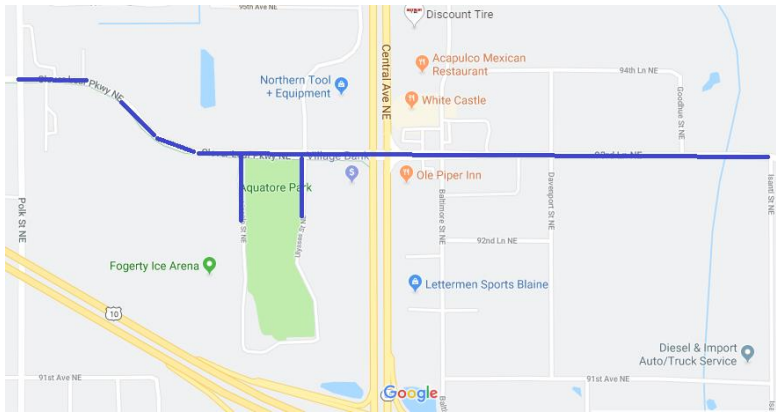

Location Map

Consultant:

**Bolton & Menk
Mike Nill**

Contractor:

Park Construction

Project Manager:

Stefan Higgins

Project Information

Major Milestones

- Project Awarded to Park Construction
- Neighborhood Notification Sent out
- Pro-construction meeting held June 4
- No work west of TH65 until after Blaine Festival

Issues

- Median to be extended - TH65 to Baltimore
- Concrete pipe production delays
- Poor soils for trail near Aquatore Park
- Coordinating Signal loops w/ MnDOT

Schedule

	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19
93rd - East of TH65					
Cloverleaf Pkwy - sidewalks					
Cloverleaf Pkwy - Road Reconstruction					

Budget Summary

Project Phase	Budget	Expense to Date	% Budget Spent
Design And Construction Support	\$ 408,545.00	\$ 113,025.00	27.7%
Construction	\$ 1,739,483.85		
Engineering, Geotech, Other			
TOTAL	\$ 2,148,028.85	\$ 113,025.00	
